



In line with government advice, the St Teresa of Kolkata Building construction site at ACU's Melbourne Campus remains open. Construction works are continuing with the implementation of COVID-19 safe protocols, procedures and strict adherence to government recommendations to ensure the health and safety of workers and others on campus.

See the latest construction progress on [webcam 1](#) and [webcam 2](#).

Project site closed Tuesday 22 December - Wednesday 13 January

Upcoming and ongoing activity: How you may be affected

Area	Impact	Timing
Mary Glowrey Building (MGB)	Front entry canopy at Victoria Parade will be demolished. To access the university, please use the Young Street entrance. Please expect changes to traffic routes during this period.	Nov 2020 - Feb 2021
Mary Glowrey Building (MGB)	The central MGB fish stair will be hoarded off and inaccessible in early 2021. Please look out for University works notification and internal signage for further details.	Jan 2021
Mary Glowrey Building (MGB)	MGB Atrium works to facilitate new services works and will involve new hoarding, structural steel grillage, scaffold, demolition and new glazing installation. Alternative access routes will be in place.	Ongoing
Mary Glowrey Building (MGB)	Service upgrade works in the MGB. Further details will be provided through university works notification.	Ongoing
Main Construction Site	Pedestrians should be aware of increased construction vehicle movement. Please expect changes to traffic and pedestrian routes with the assistance of traffic controllers.	Ongoing
Main Construction Site	Jumpform –the jumpform for the St Teresa of Kolkata Building core structure continues to climb and is currently pouring the basement level 1 core wall structure.	Ongoing
Main Construction Site	Construction of the St Teresa of Kolkata Building basement carpark structure may alter traffic arrangements.	Ongoing
Main Construction Site	A second hoist has been installed to the north face of the excavation to facilitate the transport of project personnel.	Ongoing
Main Construction Site	St Teresa of Kolkata Building basement structure works continue. The concrete structure for the basement has commenced 25 metres deep within the excavation, at basement level 7.	Ongoing
Overbuild	Overbuild works will be ongoing, including services rough-in.	Ongoing



Please expect intermittent noise during these periods

Construction update

Recent construction work includes:

- bulk excavation – complete
- anchoring works – complete
- micropiling works – complete
- overbuild services rough in – ongoing
- MGB service upgrade works – ongoing
- basement level 7 structure – commenced
- MGB Front entry canopy demolition – commenced

The latest in pictures

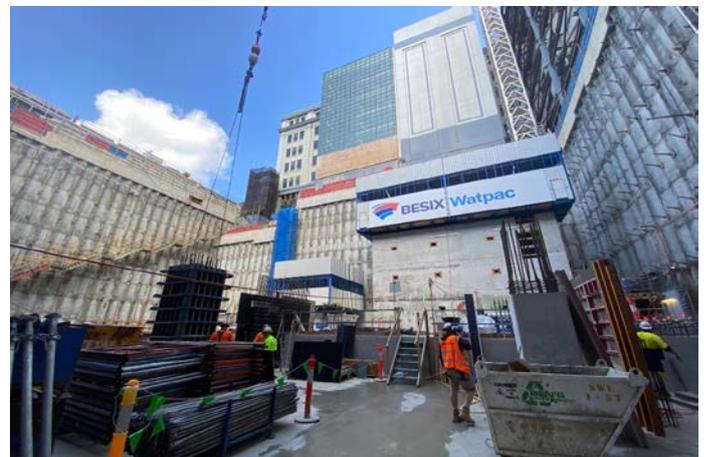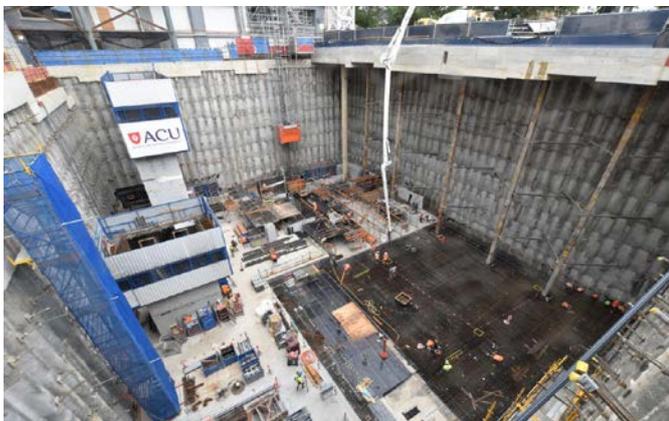

Please observe direction and safety signs and follow the instructions of Watpac traffic controllers.

If you wish to provide feedback, contact the team at ACUfeedback@watpac.com.au
