



In line with government advice, the Saint Teresa of Kolkata Building construction site at ACU's Melbourne Campus remains open. Construction works continue with the implementation of COVID-safe protocols, procedures and strict adherence to government recommendations ensuring the health and safety of workers and others on campus.

See the latest construction progress on [webcam 1](#) and [webcam 2](#).

### Four-week outlook: How you may be affected

Area	Impact	Timing
Mary Glowrey Building (MGB)	Front entry canopy at Victoria Parade will be demolished. The southern entrance will be reinstated in February following construction of a temporary gantry. To access the university before this, please use the Young Street entrance. Please expect changes to traffic routes during this period.	Nov 2020 - Feb 2021
Mary Glowrey Building (MGB)	The central MGB fish stair will be hoarded off and inaccessible in early 2021. Please look out for university works notification and internal signage for further details.	Feb

### Upcoming and ongoing activity

Area	Impact	Timing
Main Construction Site	The installation of a concrete placing boom in the basement excavation to assist with concrete pours for the main Saint Teresa of Kolkata Building structure.	Ongoing
Main Construction Site	Construction of the Saint Teresa of Kolkata Building basement carpark structure may alter traffic arrangements.	Ongoing
Main Construction Site	Pedestrians should be aware of increased construction vehicle movement. Please expect changes to traffic and pedestrian routes with the assistance of traffic controllers.	Ongoing
Main Construction Site	The jumpform for the Saint Teresa of Kolkata Building core structure continues to climb and is currently pouring the basement level 1 core wall structure.	Ongoing
Main Construction Site	Works on basement level 6 include: waterproofing and shotcreting to the retention system perimeter walls, suspended slab, walls and column pours.	Ongoing
Mary Glowrey Building (MGB)	Services upgrade work continues including library stair glazing works and lobby atrium works. This will involve new hoarding, structural steel grillage, scaffold, demolition and new glazing installation. Alternative access routes will be in place. Further details will be provided through university works notification.	Ongoing
Overbuild	Overbuild works will be ongoing, including services rough-in.	Ongoing


**Please expect intermittent noise during these periods**

## Construction update

Recent construction work includes:

- basement level 7 structure – complete
- installation of concrete placing tower – complete
- basement level 6 structure – commenced
- overbuild services rough in – ongoing
- MGB service upgrade works – ongoing
- MGB Front entry canopy demolition – ongoing

## The latest in pictures

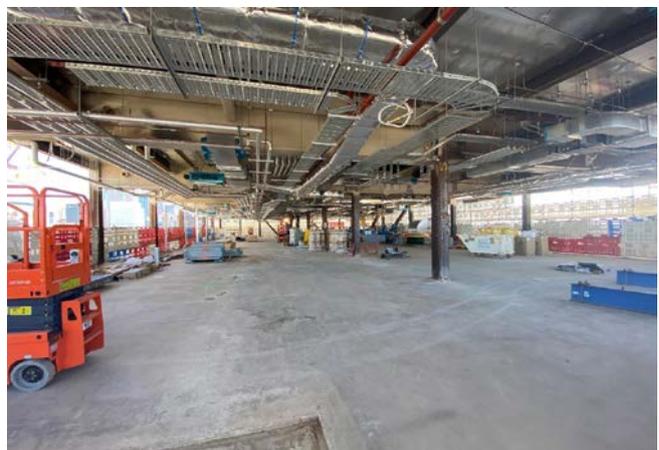

**Please observe direction and safety signs and follow the instructions of Watpac traffic controllers.**

**If you wish to provide feedback, contact the team at [ACUfeedback@watpac.com.au](mailto:ACUfeedback@watpac.com.au)**
